

MEASURE J UPDATE

Admin Council

January 14, 2019



A BETTER BC

Funded By Measure **J**




Construction Completed

Construction in Progress

Swing Space

SYMBOL KEY

- Parking Pass Dispenser
- Accessible Paths
- Bus Stop
- Under Construction

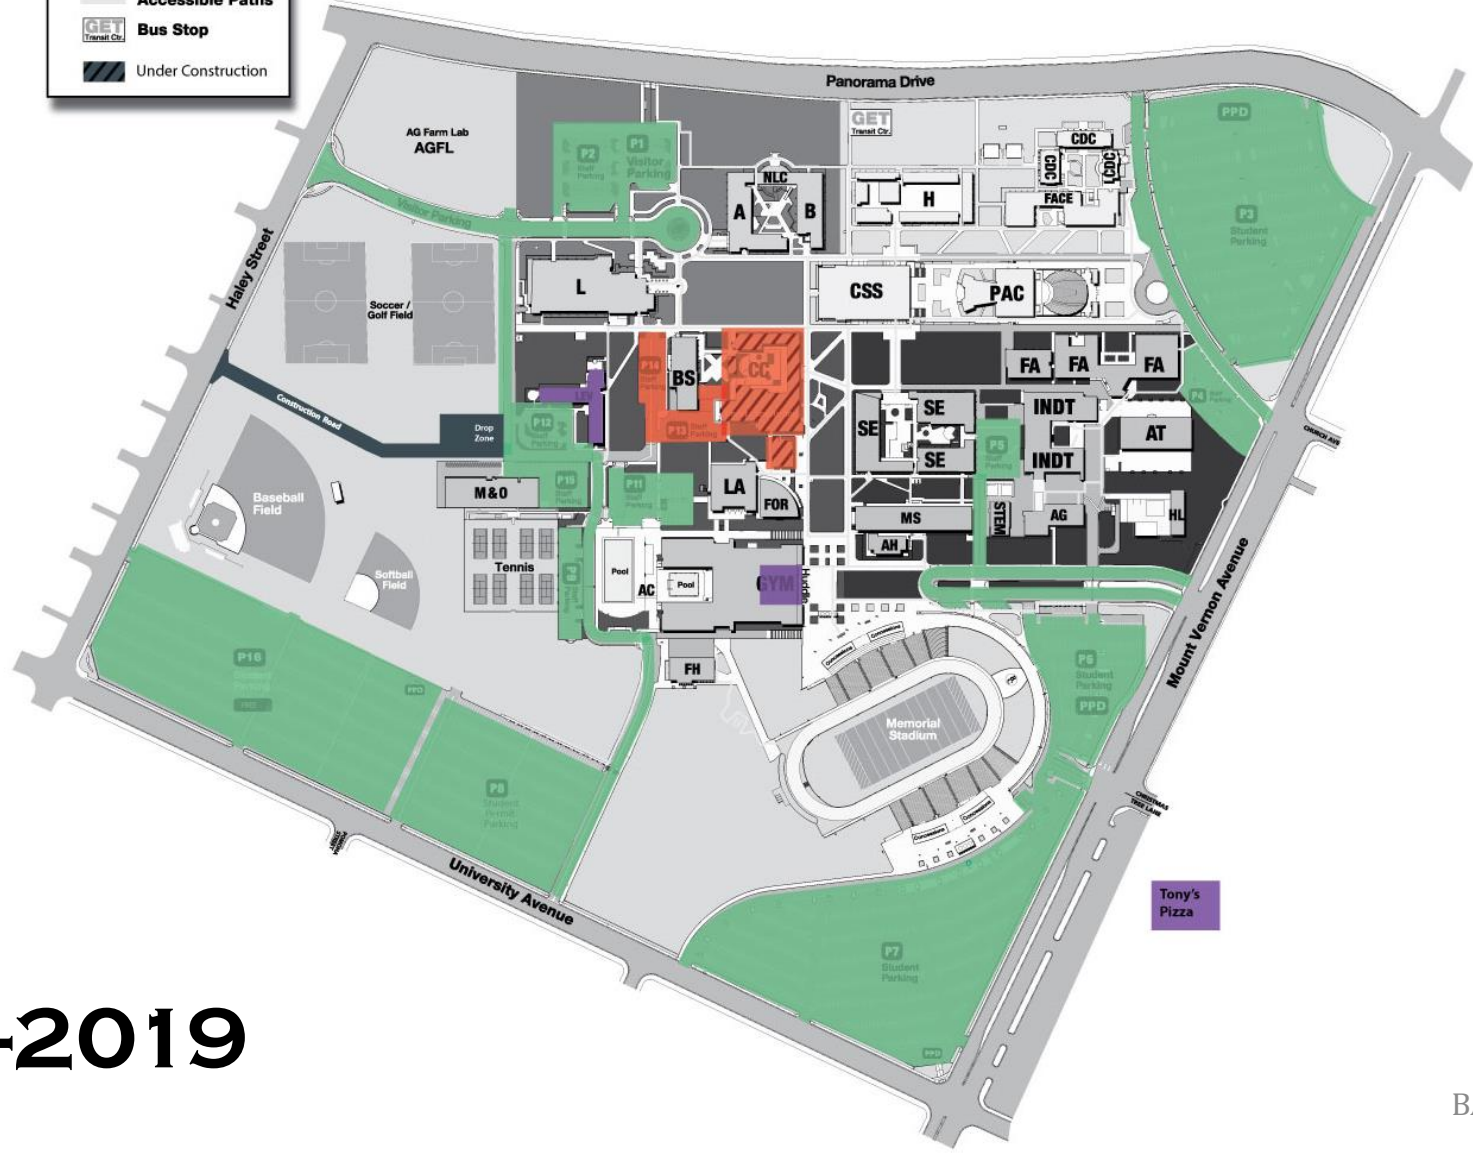

2018-2019

CURRENT MEASURE J PROJECTS



- Wireless infrastructure project
 - Evening work and will improve interior Wi-Fi on campus
 - Will be completed in February 2019

VERNON VALENZUELA VETERAN'S RESOURCE CENTER AT BAKERSFIELD COLLEGE



- VRC demolition has begun
 - Groundbreaking was November 5
 - Scheduled for completion at end of November 2019

SCIENCE & ENGINEERING BUILDING



- Bernards Bros. Construction selected as the Design-Build team
- Met with SE faculty on November 28 to discuss the build with HMC Architects
- Scheduled for completion in January 2022


GYM

- Gym
 - S.C. Anderson has been awarded the Design/Build contract
 - Scheduled for completion in December 2022



STADIUM

- Stadium
 - To be done in two phases
 - Phase 1
 - March 2019-August 2019
 - Phase 2
 - January 2020-August 2020

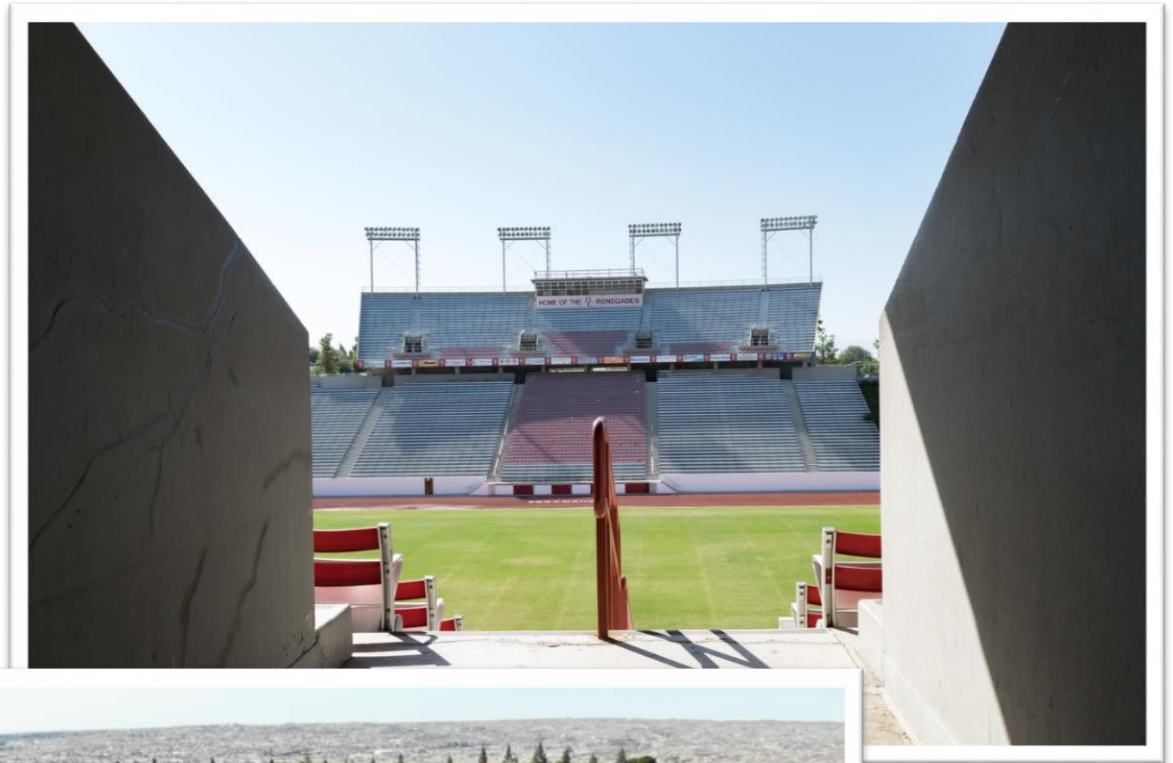

CAMPUS CENTER



- A few Campus Center offices moved to LEV in October
- Demolition of Campus Center began in December 2018
 - Groundbreaking **Wednesday, January 16, 2019**
 - Scheduled for completion in mid-November 2020

OTHER PROJECTS

Parking Lots

Arvin Campus

Infrastructure

Campus Signage

Swing Space



SPECIFIC PROJECT QUESTIONS??



Tamara Baker
Program Manager - Community Relations
Tamara.baker@bakersfieldcollege.edu
(661) 395-4910



Bill Potter
Director, Facilities, Maintenance and Operations
William.Potter@bakersfieldcollege.edu
(661) 395-4478

