

# FACILITIES UPDATE

College Council

February 1, 2019



**A BETTER BC**

Funded By Measure **J**




Construction Completed

Construction in Progress

Swing Space

**SYMBOL KEY**

- Parking Pass Dispenser
- Accessible Paths
- Bus Stop
- Under Construction

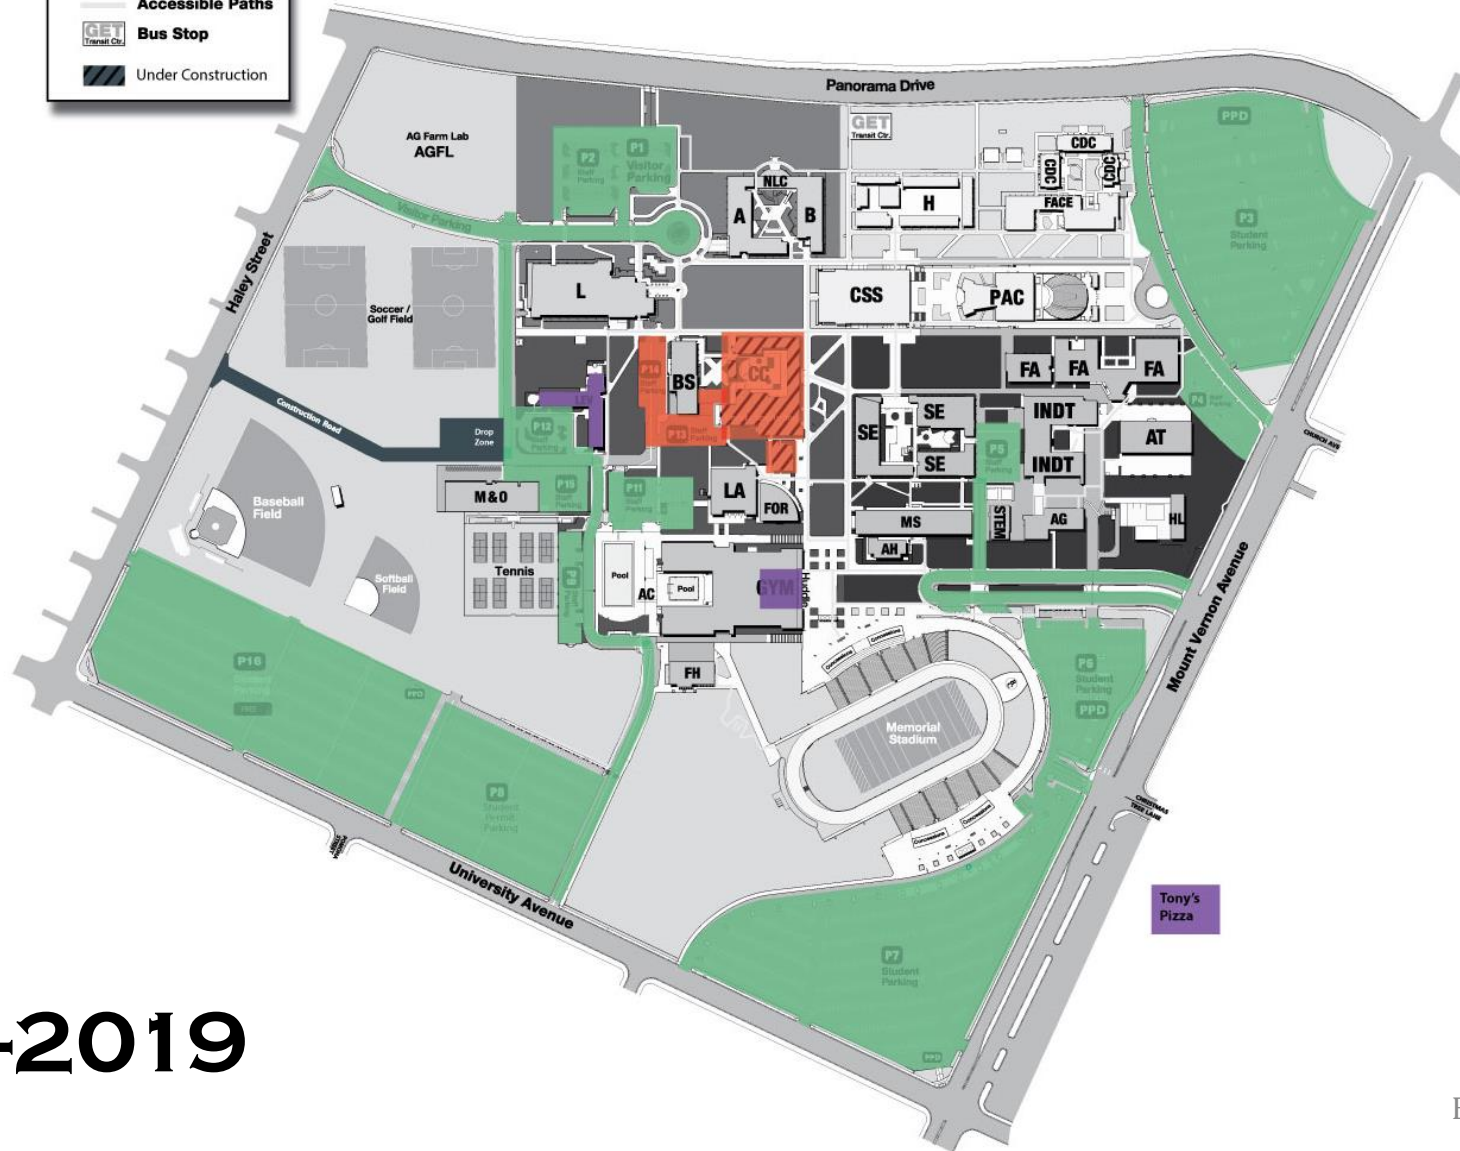

2018-2019

# CURRENT MEASURE J PROJECTS



- Wireless infrastructure project
  - Evening work and will improve interior Wi-Fi on campus
  - Will be completed in February 2019

# VERNON VALENZUELA VETERAN'S RESOURCE CENTER AT BAKERSFIELD COLLEGE



- VRC demolition has begun
  - Groundbreaking was November 5
  - Scheduled for completion in December 2019



# SCIENCE & ENGINEERING BUILDING



- Bernards Bros. Construction selected as the Design-Build team
- Met with SE faculty on November 28 and January 7 to discuss the build with HMC Architects
- Scheduled for completion in January 2022


# GYM

- Gym
  - S.C. Anderson has been awarded the Design/Build contract
  - Schematic Design Kick Off on December 5
  - Scheduled for completion in December 2022



# STADIUM

- **Phase 1**
  - Artificial turf and track replacement
    - **March 2019-August 2019**
- **Phase 2**
  - Renovations to restrooms, concession stands, and press box. Also, replacement of score board, PA system and field lighting.
    - **January 2020-August 2020**

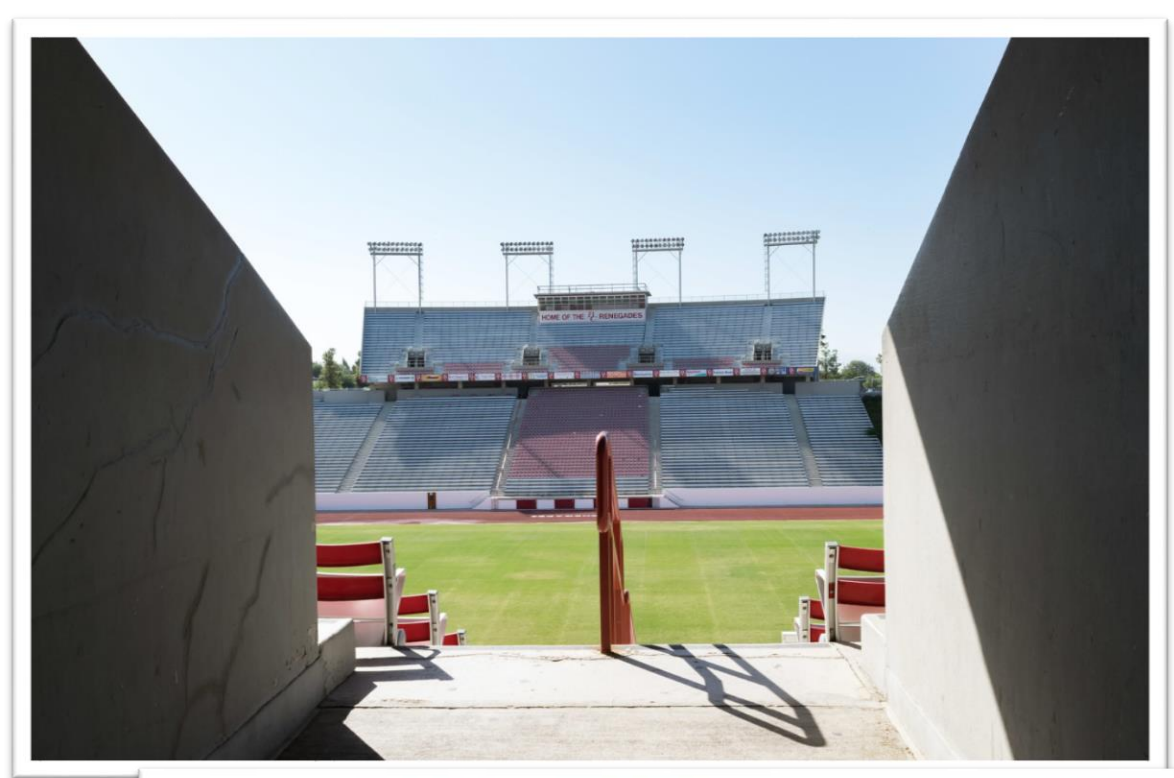

# FOOD SERVICES

- Huddle and Mount Vernon Commissary (MVC)
  - Kitchen moved during Winter Recess
- Food Services now in the Huddle
- Will have BC food truck on campus serving food named “Gades Grub”





# CAMPUS CENTER



- Some Campus Center offices moved to LEV in October
  - Student Life, BCSGA, Veterans Resource Center, Health Center
- Demolition of Campus Center began in December 2018
  - Groundbreaking January 16
  - Scheduled for completion in mid-November 2020

# INFRASTRUCTURE

- Will take place over the course of the Measure J project schedules



- Total of nine (9) small projects
  - Campus water pressure and lines
  - Thermal tank
  - EMS system and building meters (water, gas, power)
  - Sewer lines
  - Modifications and repairs to the northeast corner of campus
  - Security cameras/Data/Fiber
  - High voltage electrical
  - Storm Drain
  - Gas lines

# OTHER PROJECTS

- Parking lots
  - Close Out Phase (all lots completed)
- Arvin Campus
  - Programming phase
  - Currently performing surveys at the donated land
- Campus Signage
  - Programming phase
  - Installing monument signage on the four corners of Bakersfield College: Haley & University, University & Mount Vernon, Mount Vernon & Panorama
- Swing Space
  - Temporary classroom and office space for programs to use as they are moved for Measure J projects
  - Various phases, but to date have completed projects at LEV, Huddle & MVC



# SPECIFIC PROJECT QUESTIONS??



Tamara Baker  
Program Manager - Community Relations  
[Tamara.baker@bakersfieldcollege.edu](mailto:Tamara.baker@bakersfieldcollege.edu)  
(661) 395-4910



Bill Potter  
Director, Facilities, Maintenance and Operations  
[William.Potter@bakersfieldcollege.edu](mailto:William.Potter@bakersfieldcollege.edu)  
(661) 395-4478
